


Second laser acceptance test at Photonics

Power calibration

with a unterminated coupling trigger cable on the DG 535
which make the power a bit higher of 8 mW

New DP2 laser calibration

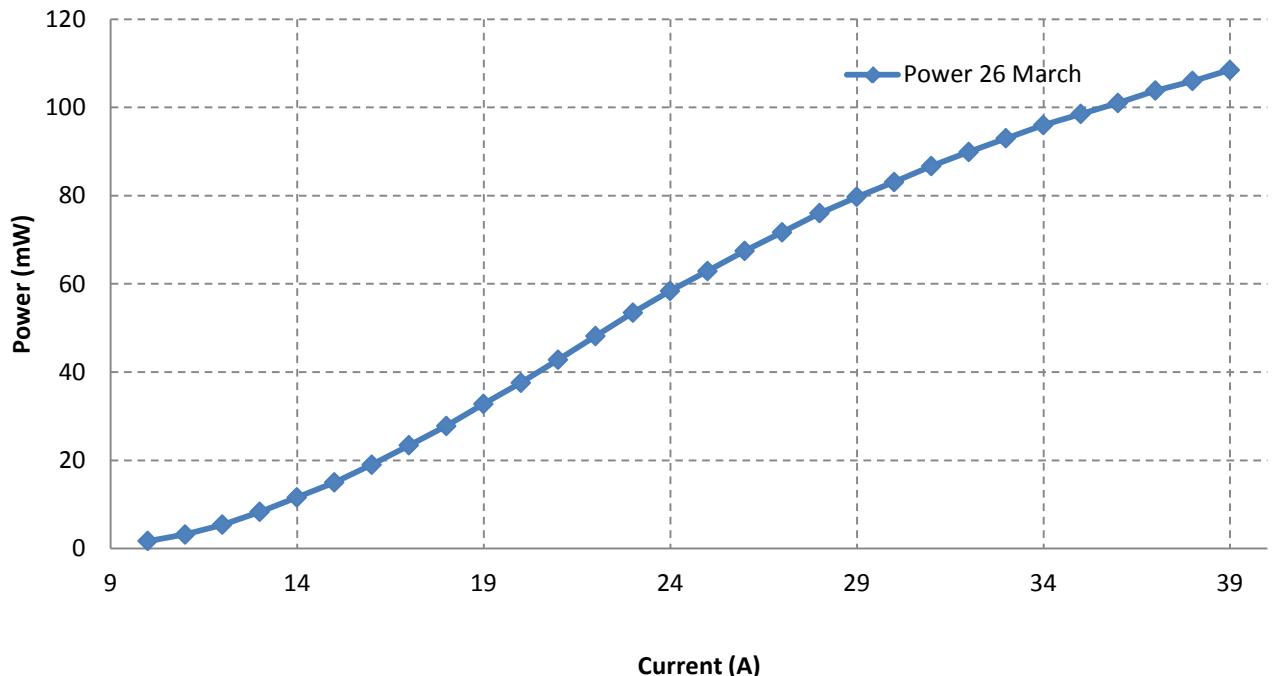

Current (A)	Power 26 March	T	
8.5		27	71.7
10	1.7	28	76
11	3.2	29	79.7
12	5.4	30	83.1
13	8.3	31	86.7
14	11.6	32	89.9
15	15	33	93
16	19	34	96
17	23.4	35	98.5
18	27.8	36	101
19	32.8	37	103.8
20	37.6	38	106
21	42.8	39	108.5
22	48.2		
23	53.5		
24	58.4		
25	62.9		
26	67.5		
